

DRIFTSRAPPORT

Månedssrapport Januar 2019

Faurbo Vandværk

1/2



MÆNGDER

TOTAL INDVUNDET	2058,36 m ³
Boring 1	1073,74 m ³
Boring 2	984,62 m ³
TOTAL UDPUMPET	1888,72 m ³
Udpumpning	1888,72 m ³
TOTAL SKYLLEVAND	0,00 m ³
Skyllevand	0,00 m ³

ELFORBRUG




ELFORBRUG	
Samlet proces	2560 kWh
Delproces / udpumpning	848 kWh



NATFORBRUG

Vandforbrug mellem klokken 02.00 og 04.00

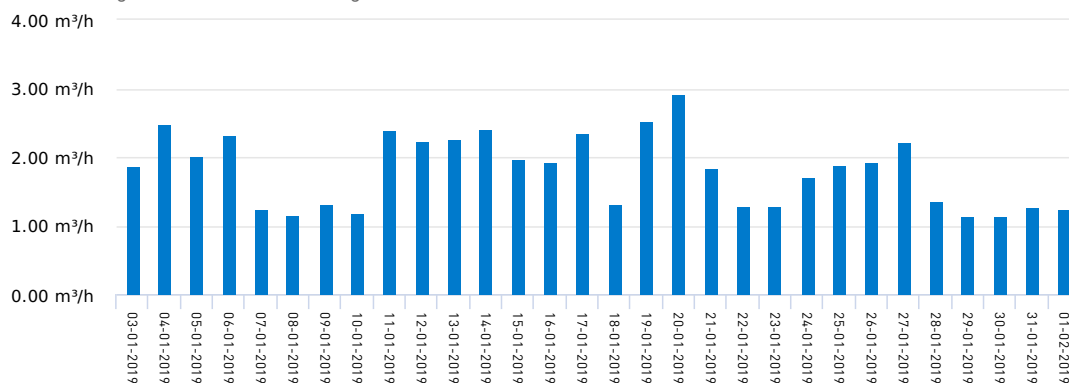

FILTRE

Filter 1	4 skyl
Filter 2	4 skyl
Filter 3	6 skyl
Filter 4	6 skyl

DRIFTTIMER



BORINGER	
1	118 timer
2	143 timer
PUMPER	
1	364 timer
2	380 timer
FILTERMOTOR	
1	261 timer
2	1 timer



Blue Control®
BC7000

DRIFTSRAPPORT

Månedssrapport Januar 2019

Faurbo Vandværk


2/2



NIVEAUER I BORINGER

BORING	HØJEST	LAVEST	SÆNKNING	MÆNGDE
1	-49,15 m	-54,06 m	4,91 m	1073,74 m ³
2	-49,38 m	-53,31 m	3,93 m	984,62 m ³

Fordeling for indvundet vand

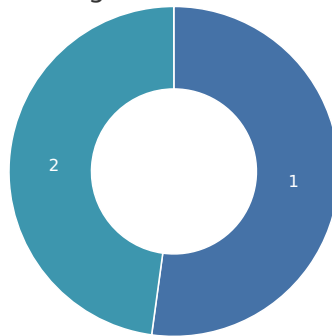

● Boring 1 : 52.2%
● Boring 2 : 47.8%



Blue Control®
BC7000
