


Faurbo Vandværk

Månedsrapport 01-2018

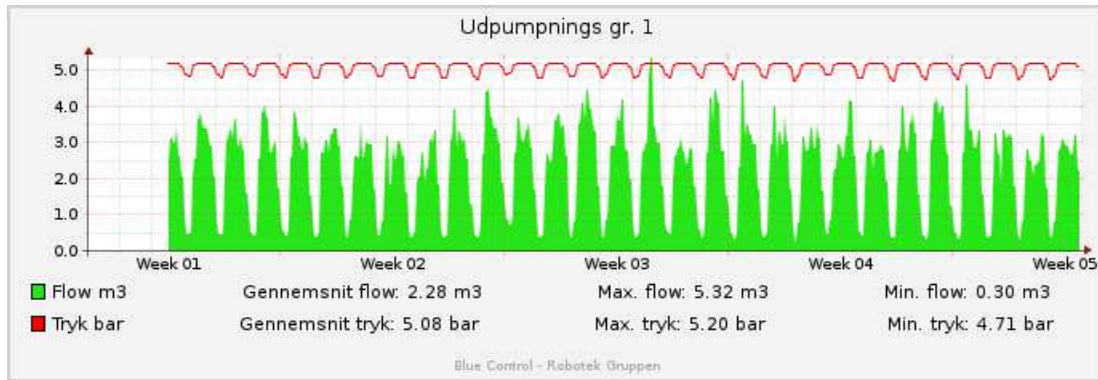

Mængder

Udpumpet vandmængde:	Total:	1.715,9 m ³	Måler 1:	1.715,9 m ³
Indvundet vandmængde:	Total:	1.766,6 m ³	Måler 2:	1.766,6 m ³

Forbrug

Elforbrug:	Total:	1.905,2 kWh	Udpumpet:	802,0 kWh
	Total:	1,11 kWh/m ³	Udpumpet:	0,47 kWh/m ³

Flow

Flow måler 1:

Min. Flow:	0,00 m ³ /h	Tidspunkt: 01-01-19 00:00:00
Max. Flow:	13,55 m ³ /h	Tidspunkt: 02-01-18 03:09:37

Flow måler 2:

Min. Flow:	0,00 m ³ /h	Tidspunkt: 01-01-19 00:00:00
Max. Flow:	14,78 m ³ /h	Tidspunkt: 03-01-18 10:03:41

Niveauer i boringer:

Boring 1 niveau:	Højest:	-47,99 m	Lavest:	-53,40 m	Sænkning:	5,41 m
Boring 2 niveau:	Højest:	-47,31 m	Lavest:	-53,59 m	Sænkning:	6,28 m

Filter:

Filter 1:	Antal skyl:	5
Filter 2:	Antal skyl:	5
Filter 3:	Antal skyl:	10
Filter 4:	Antal skyl:	10

Drifttimer:

	Periode:	Total:
Boring 1:	91 Timer	4003 Timer
Boring 2:	132 Timer	6854 Timer
Pumpe 1:	355 Timer	14875 Timer
Pumpe 2:	368 Timer	14893 Timer
