

DRIFTSRAPPORT

Månedsrapport Februar 2023

Faurbo Vandværk

1/2



MÆNGDER

TOTAL INDVUNDET	1909,59 m ³
Boring 1	960,31 m ³
Boring 2	949,28 m ³
TOTAL UDPUMPET	1880,36 m ³
Udpumpning	1880,36 m ³
TOTAL SKYLLEVAND	6,65 m ³
Skyllevand	6,65 m ³

ELFORBRUG




ELFORBRUG	
Samlet proces	1921 kWh
Delproces / udpumpning	744 kWh



NATFORBRUG

Vandforbrug mellem klokken 02.00 og 04.00

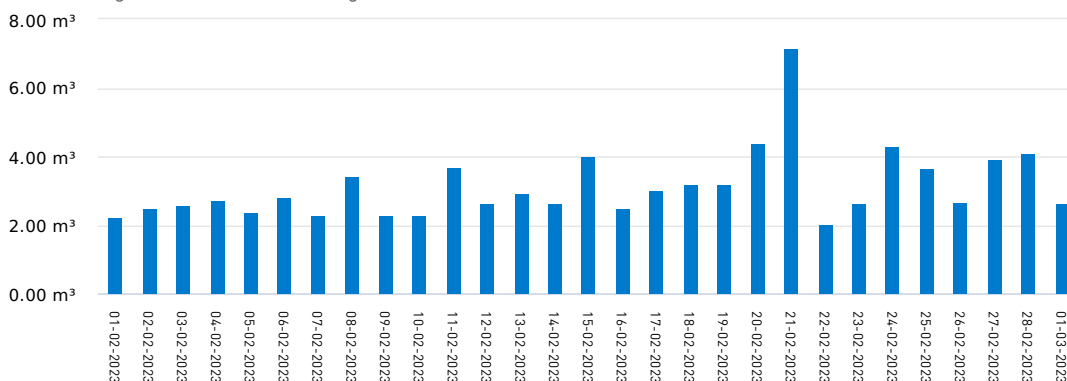

FILTRE

Filter 1	5 skyl
Filter 2	5 skyl
Filter 3	7 skyl
Filter 4	7 skyl

DRIFTTIMER



BORINGER	
1	119 timer
2	117 timer
PUMPER	
1	336 timer
2	336 timer
FILTERMOTOR	
1	236 timer
2	1 timer



Blue Control®
BC7000

DRIFTSRAPPORT

Månedsrapport Februar 2023

Faurbo Vandværk


2/2



NIVEAUER I BORINGER

BORING	HØJEST	LAVEST	SÆNKNING	MÆNGDE
1	-48,92 m	-53,39 m	4,46 m	960,31 m ³
2	-48,89 m	-53,43 m	4,54 m	949,28 m ³

Fordeling for indvundet vand

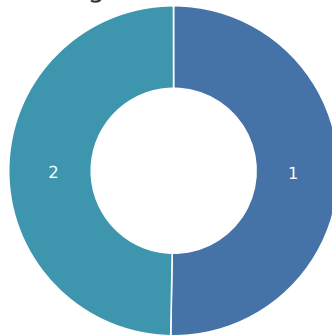

● Boring 1 : 50.3%
● Boring 2 : 49.7%



Blue Control®
BC7000
